

# Public Exhibition for the S278 Highway Improvements Linked to the Wyre Meadows Residential Development in Station Road, Pershore

Welcome to this public exhibition, Persimmon Homes have invited local residents and businesses to helpfully engage and explain the highway improvement works that are required as part of both planning permissions for the Wyre Meadows residential developments.


The following boards should expand on the highway works involved, timings of the road closures, and diversions that will be put in place and the timings schedule.



#### FIRST STAGE — PUFFIN CROSSING ON STATION ROAD

The first stage of works will involve erecting a puffin crossing opposite Pershore High School, as shown in the plans below.


These works will commence from 2nd July 2018 and finish by 23rd August 2018. This will entail a road closure, in place from Saturday 21st July until Thursday 23rd August along Station Road. At this time a diversion route will be in place, which is shown in blue on the plan on board 2. Please note businesses and properties along the closure route will still be able to gain access to frontages and pedestrian access will be feasible throughout the road closure.

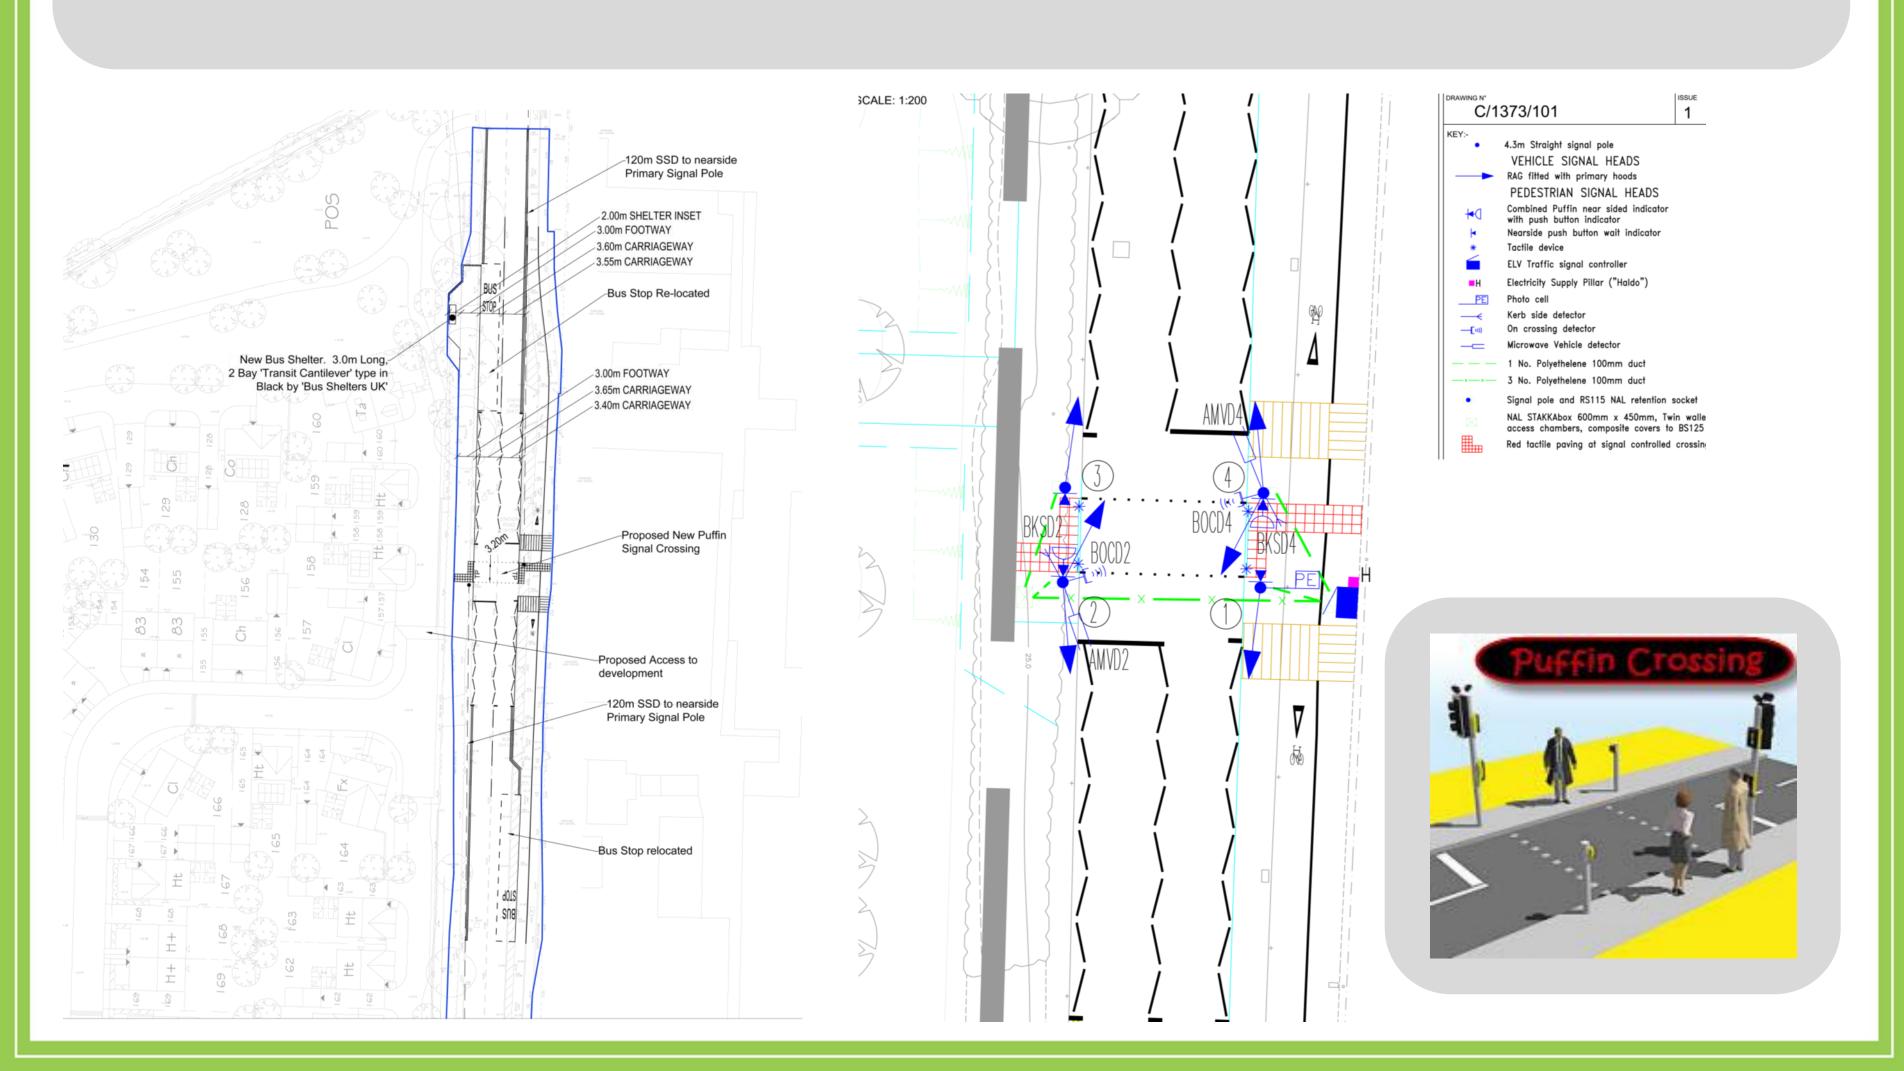



## STATION ROAD CLOSURE & DIVERSION ROUTE (21ST JULY UNTIL 23RD AUGUST 2018)

Please note businesses and properties along the closure route will still be able to gain access to frontages and pedestrian access will be feasible throughout the road closure.

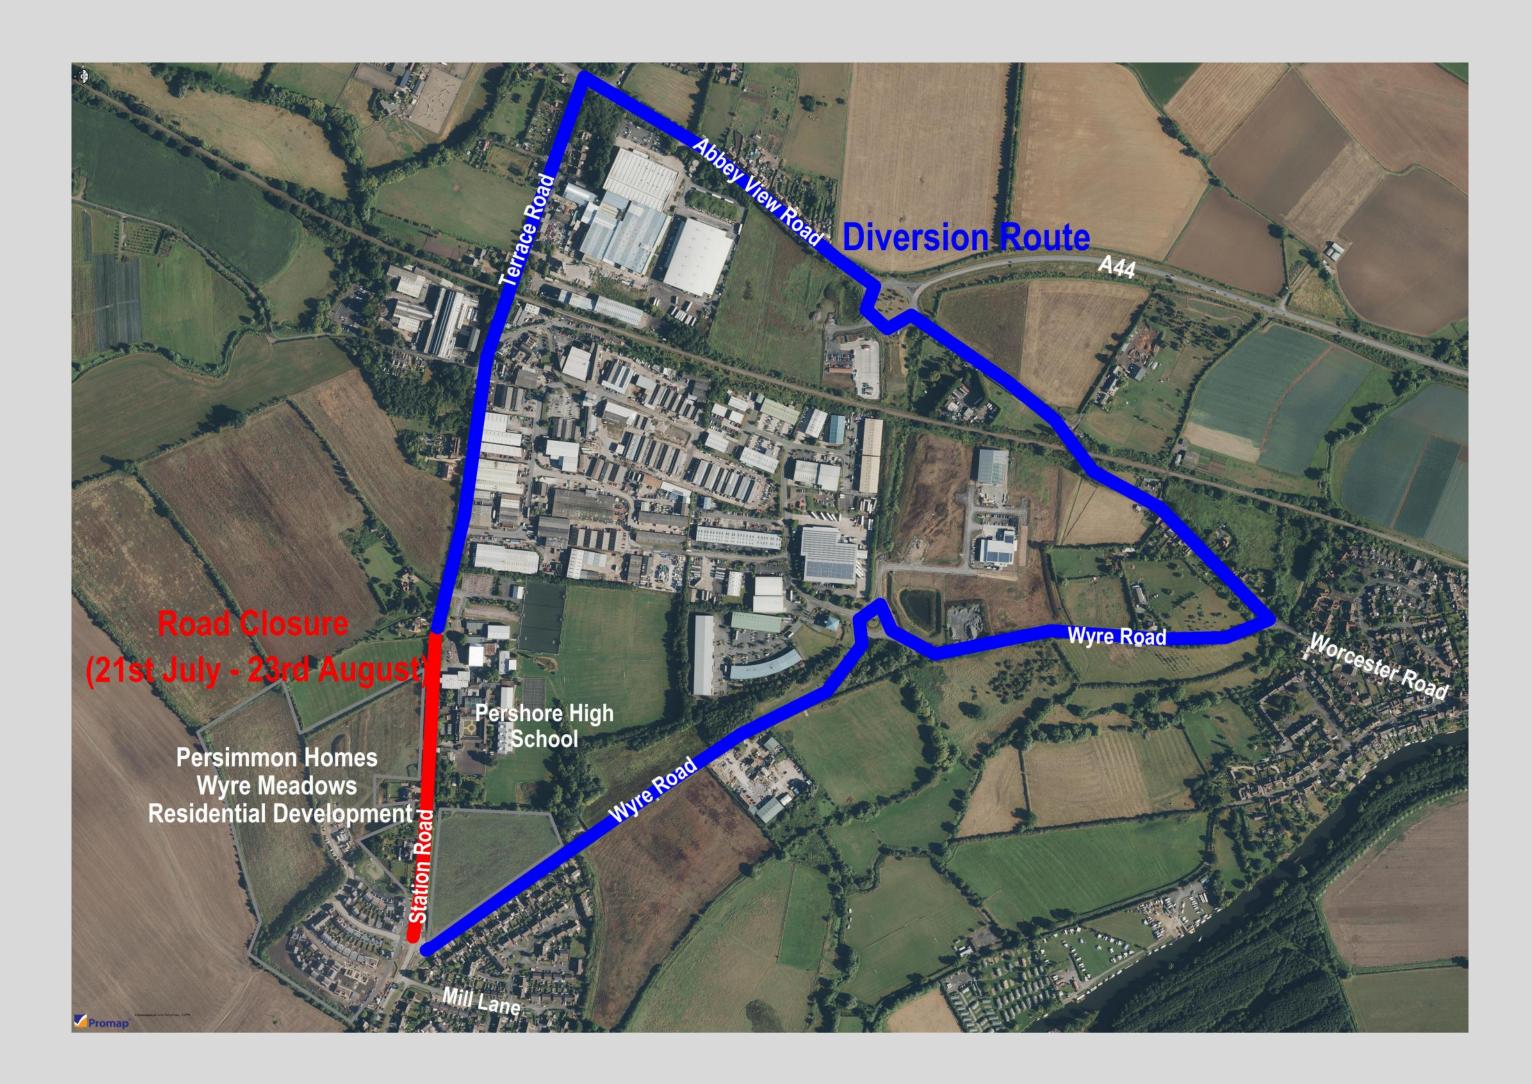


#### SECOND STAGE — DRAINAGE OUTFALL WORKS

The second stage of works will involve completing the drainage outfall works, which will commence on 23rd July 2018 and complete by the 3rd August 2018 these works will be done under the same road closure as listed on the first board.

### FINAL STAGE — ERECTION OF PERMANENT TRAFFIC LIGHTS AT WYRE / STATION ROAD JUNCTION

The final set of works will take place from 28th August 2018 until 21st December 2018 (subject to any unforeseen circumstances) this will enable the existing temporary lights to be removed and the permanent 4-way traffic lights to be erected. In this period we will be widening the existing highway and building pedestrian crossing points, as shown in the plan below. We will also plane and re-lay the existing highway surface. We will endeavour to complete all the works under the four-way lights, but there will be a period during October Half Term where Wyre Road will be shut for the 5 business days of Half Term. Please refer to the plan on board 3 to show the extent of the road closure and the diversion route that will be in place during this time. It may be necessary to carry out a further road closure of Station Road, to carry out the final resurfacing works at the Wyre Road junction. If this is required then contact will be made with those affected separately and information boards will be displayed in advance of this.



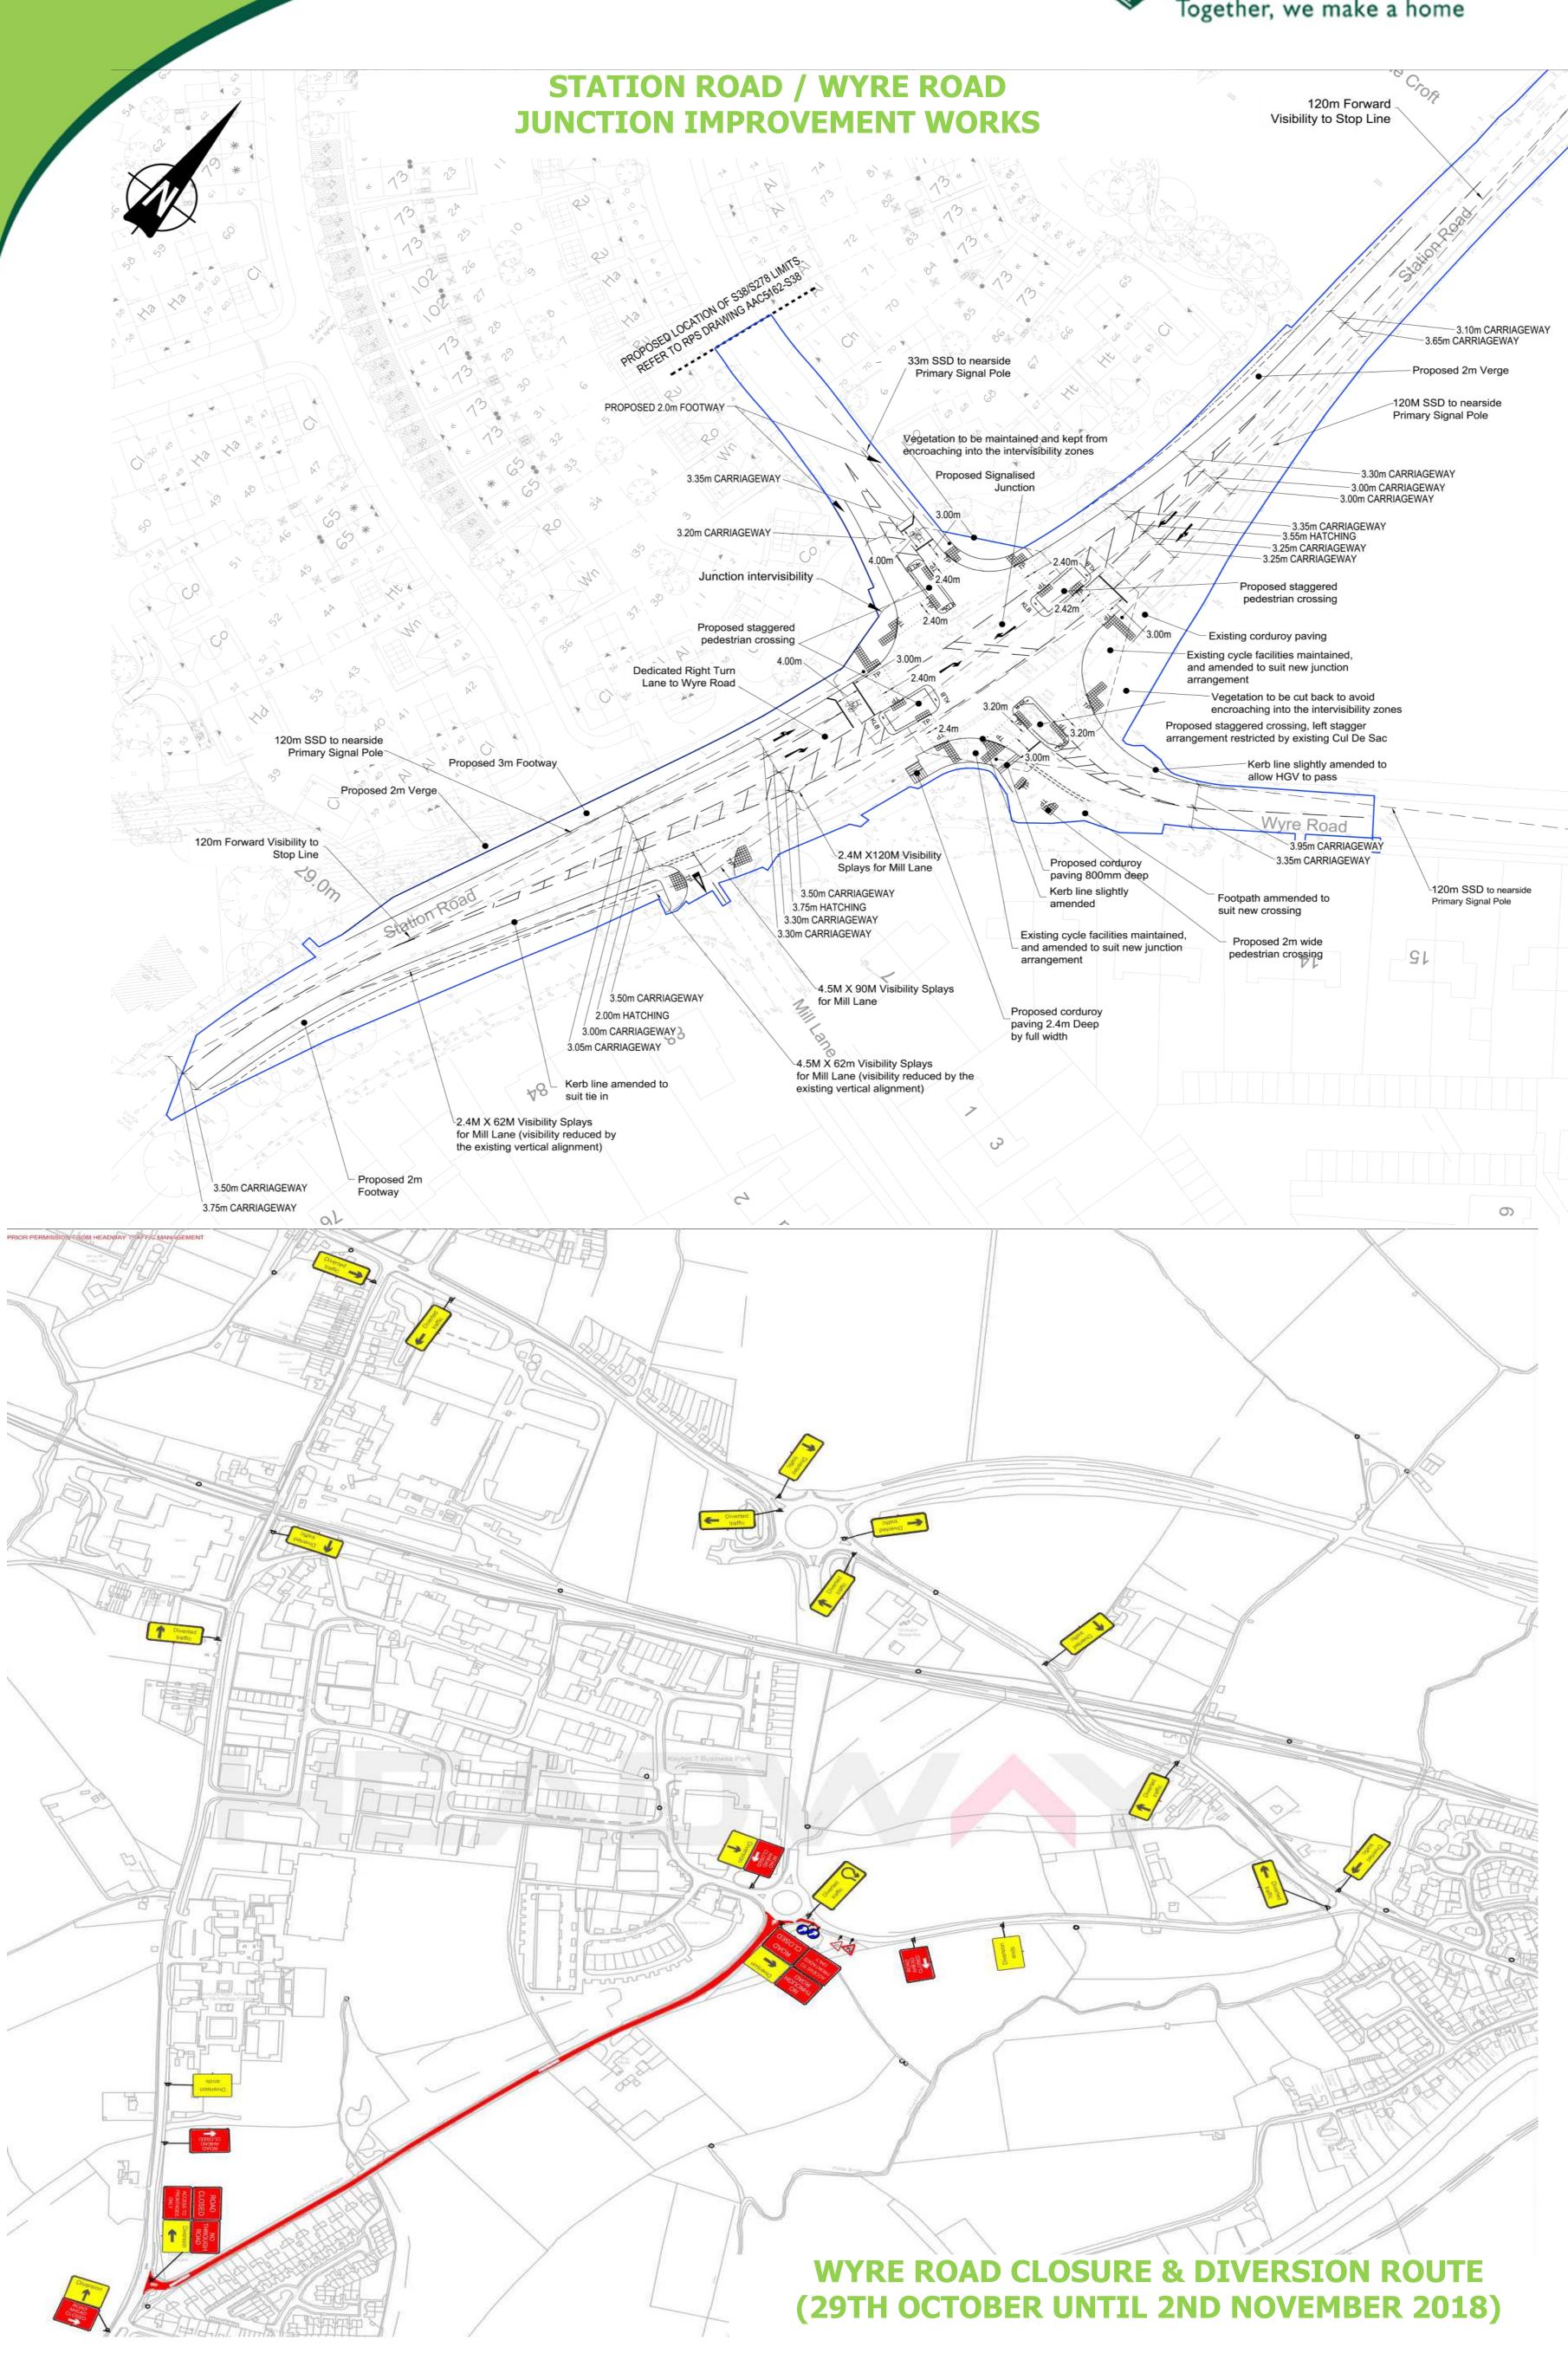



#### **FULL PROGRAMME OF WORKS & TIMETABLE**

We have worked closely with Worcestershire County Council and Wychavon District Council to produce the programme below. Please note that the programme is subject to change due to the complexities and unknowns of what may be uncovered during the works.

Birmingham Email:												: (0121) 693 7	21) 708 5000 121) 693 7662 enquiries@mvkelly.co.uk ww.mvkelly.co.uk																
	Civil Engineering & Building Contractors Client Site Description of Works		Persimmon Homes South Midlands Station Rd, Pershore Phase S278 Works															Date of Programme Program Revision Completed by <u>Key</u>			C Sam Pinches / Reece McCarthy MVK Tasks Streetlighting Contractor (Not MVK) Plum Festival School Holidays								
	ANTICIPATED WORKS SCHEDULE:			Week No:	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25
		Month: Week Commencing:			2	July 9 16 23		30 6		Augus	13 20 27		2 1	September 3 10 17		24 1		October 8 15		22			Novem 12			December   3   10   17			
		Duration	Start	Finish		9	10	23	30	-	13	20	1		10	- 17	24	•	•	13	22	23	3	12	19	20		10	11
	S278 Works - Pelican Crossing																												
	<u>Drainage</u>	<u>6wks</u>	02/07/18	10/08/18	i i																								
	SMH01 to footpath (2-Way Lights) - Gang 1	5d	02/07/18	06/07/18																									<b>↓</b>
	SMH03 to footpath (Footpath Closure) - Gang 1	10d	09/07/18	20/07/18									-																
1c	Culvert to SMH03 (Road Closure) - Gang 1	15d	23/07/18	10/08/18																									+
2	Road / Footpath / Crossing Works	6wks	21/07/18	23/08/18																									
	Kerbing Works	5d	21/07/18	26/07/18																									
	Footpath Works	15d	23/07/18	10/08/18																									
	Planning off works	4d	07/08/18	10/08/18																									
	Pelican Crossing and associated works	4d	13/08/18	16/08/18																									
	Surfacing footpaths / roads / white lining / tactiles	5d	17/08/18	23/08/18																									
	RSA3 and PCC Inspection	1d	24/08/18	24/08/18																									
2g	Commissioning	1d	28/08/18	28/08/18																									
																													/
	Site Outfall Works	2wks	23/07/18	03/08/18																									/
	<u>Drainage</u>																												/
3a	Phase 2 to Culvert Drainage (Road Closure) - Gang 2	10d	23/07/18	03/08/18								$\vdash$																	
	0070 Waster A Wass Classel	+										$\overline{}$																	+
	S278 Works 4-Way Signals	47	00/00/40	04/40/40						-	-												n						
	S278 Works 4-Way Signals Footpath works - 1 x side	17wks 24d	<b>28/08/18</b> 28/08/18	<b>21/12/18</b> 28/09/18								-						-								, -			
	Carriageway widening - 1 x side	20d	17/09/18	12/10/18						-	<del>                                     </del>																		+
	Ducting Works	15d	08/10/18	26/10/18																									+
	Build-Out 1&2 - Station Road Singe Lane Closure	5d	22/10/18	26/10/18																y.									
	Build-Out 3&4 - Wyre Road Closure (Half Term)	5d	27/10/18	02/11/18																							$\overline{}$		
	Footpath works - Wyre Road Tactile Crossing	5d	31/10/18	05/11/18																									
	Traffic Signals Installation	5d	05/11/18	02/11/18																									
	Footpath works - Opposite side	15d	05/11/18	23/11/18																									
4i	Carriageway widening - Opposite side	10d	19/11/18	30/11/18																									
4j	Surfacing footpaths / tactiles	5d	03/12/18	07/12/18																									
	Surfacing roads / white lining	5d	10/12/18	14/12/18																									4
41	Snagging Works / Final Inspection	5d	17/12/18	21/12/18																									
	Chrochlimbing	1											-																+
	Streetlighting Streetlights Installation and WPD	12d	24/09/18	30/10/18			<del>                                     </del>																						+
	Street lights installation (site side)	5d	24/09/18	28/09/18									-																+
	Street lights installation (site side)  Street lights installation (opposite side)	5d 5d	22/10/18	26/10/18																									+
	WPD energising	2d	29/10/18																		8								+
			20/10/10	55/15/10																									

#### **OTHER MATTERS**

Communicating to the local community and motorway users?

Expanding on the reason for no roundabout?

Any other points to raise / explain?

Thank you again for taking the time to attend this public exhibition we hope that it has been useful. We appreciate that these works will cause some degree of disruption and we greatly appreciate your patience during this time.

Thank you for attending today's event if you have any further questions or concerns please speak to one of our representatives at the event today or feel free to email <a href="mailto:smidconsultation@persimmonhomes.com">smidconsultation@persimmonhomes.com</a>
